L2 stays on 3 Nov only if flushing starts 24 Oct on municipal water and PAHU takes option B; otherwise 8 Nov

K2 building L2 systems commissioning, 12 MW. Status as at 18 Oct against the 3 Nov date in K2's RFS of 30 Sep

6 of 10 L2 items are done against the original plan date of 20 Oct. The 4 open items are opposite; only flushing is on the critical path.

K2 has said 3 Nov cannot move: the client's L3 witness team arrives 10 Nov.

Both conditions are settled this week. GC (Jason) answers on the water source on 21 Oct. We ask K2 to confirm PAHU option B by the same date.

If either condition fails, our estimate is 8 Nov.


Open item	Position at 18 Oct	Closes	Owner
Chilled-water flushing	**GC update 17 Oct: start 24 Oct. Water source (municipal or truck) still open**	**2 Nov**	**GC (Jason)**
PAHU FAT	Vendor rig limited to 88 kW; K2 requires 120 kW full load. Option B proposed	At SAT	Vendor, K2
UPS paralleling	Vendor engineer on site 22 Oct, 2 days	23 Oct	Vendor
EPMS points list	312 points unconfirmed; chased twice by 15 Oct	Pending NV5	NV5

Source: GC update 17 Oct; K2 RFS 30 Sep; Allstewards site status 18 Oct

Confidential. Prepared for K2 project management

Flushing from 24 Oct ends 2 Nov with one day of float; a water truck adds 3 days and misses 3 Nov

Chilled-water flushing chain, calendar days, 18 Oct to 10 Nov

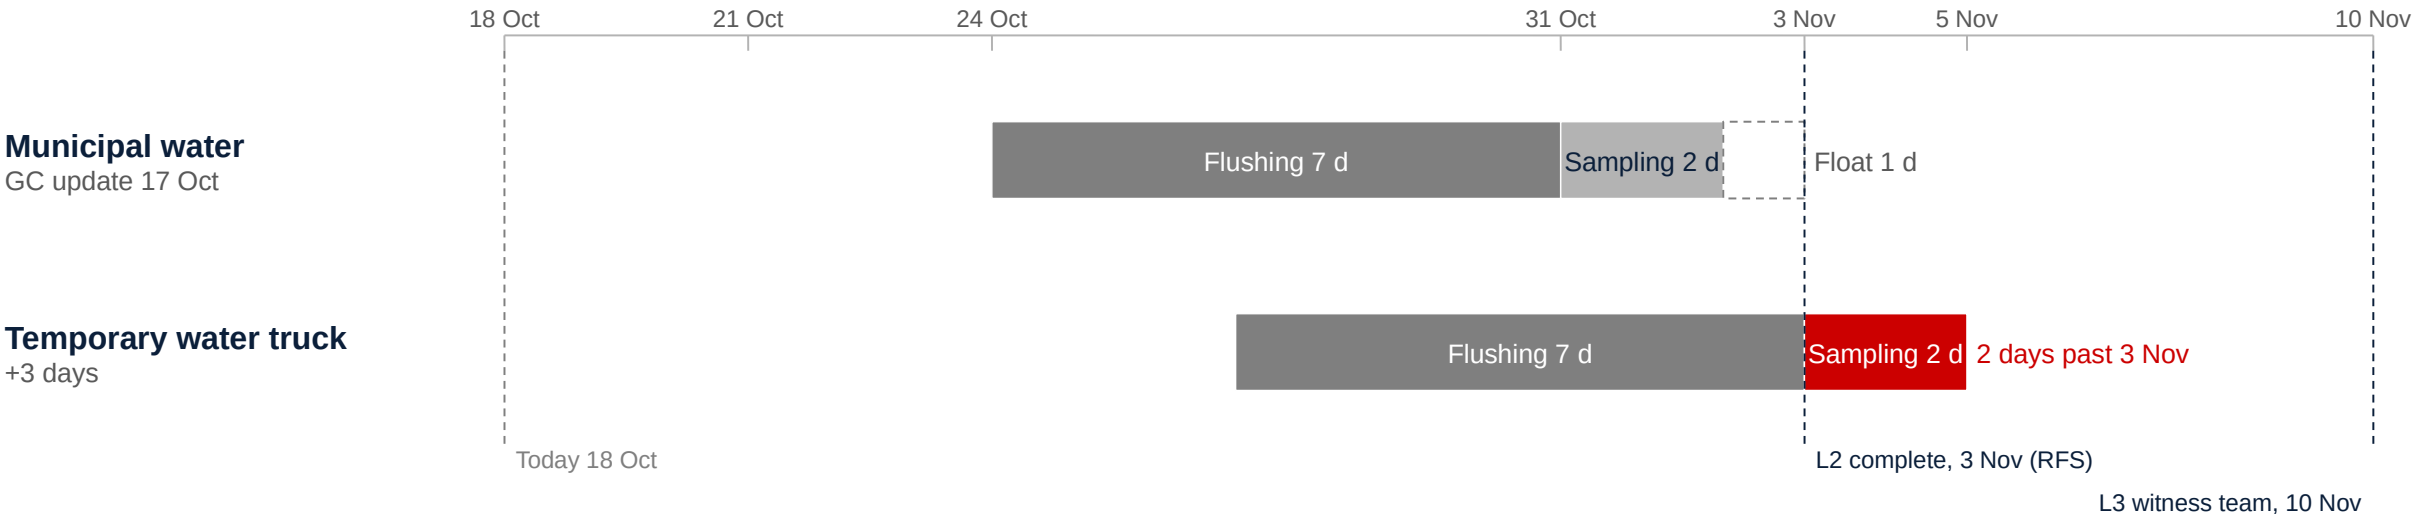

Flushing takes 7 days and water-quality sampling 2 days. Starting 24 Oct, the chain ends 2 Nov, one day before the 3 Nov date.

The water source is still open; a temporary water truck instead of municipal supply adds 3 days and ends 5 Nov. GC (Jason) answers on 21 Oct.


K1 L2 slipped 9 days at the same time last year, also on flushing.

Source: GC update 17 Oct; K2 RFS 30 Sep; K1 L2 record; Allstewards analysis

Confidential. Prepared for K2 project management

Option B keeps PAHU FAT on 3 Nov at no cost; option A at the Rayong lab adds two weeks and THB 180,000

PAHU factory acceptance test: vendor rig capacity against the K2 full-load requirement, kW

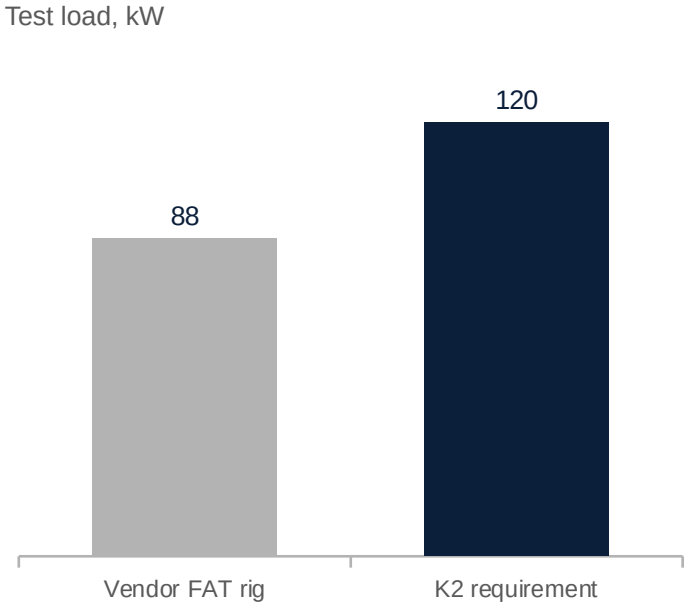

Rig falls 32 kW short of the full-load test the K2 specification calls for

	Option A: third-party lab, Rayong	Option B: calculation check, dew point verified at SAT
What is tested	Full 120 kW load on the lab rig	Vendor calculation checked at 120 kW; dew point verified on site under load
Schedule effect	+2 weeks	None
Cost	+THB 180,000	None
Who	Vendor, Rayong lab	Vendor, Allstewards at SAT
Effect on 3 Nov	Missed	Held
Our view	**Not recommended**	**Recommended; needs K2 acceptance by 21 Oct**

We recommend option B. It is the only route that keeps 3 Nov, and the dew-point check at SAT is done under real site load rather than a lab rig.

Source: PAHU vendor (rig limit 88 kW); K2 PAHU specification (120 kW); vendor quotation for the Rayong test

Confidential. Prepared for K2 project management

UPS paralleling closes 23 Oct; EPMS waits on NV5, which has not confirmed 312 points after two chasers

The two remaining L2 items outside the flushing chain, position at 18 Oct

Item	Remaining work	Depends on	Date	Owner
UPS paralleling	Parallel operation test with the vendor engineer on site, 2 days	Vendor engineer arrival 22 Oct (confirmed)	22 to 23 Oct	Vendor
EPMS points list	**312 points still to be confirmed before the points list can be signed off**	**NV5 reply; chased twice by 15 Oct, no date given**	**Pending NV5**	**NV5**

UPS paralleling has no open dependency and sits inside the flushing window; it does not affect 3 Nov.

The EPMS points list is the one item waiting on a third party with no date. Two chasers from Allstewards have not produced the 312 confirmations.

We ask K2 to raise the 312 points with NV5 directly by 24 Oct, so the list is closed before flushing ends on 31 Oct.

Source: UPS vendor site schedule; Allstewards correspondence with NV5 to 15 Oct

K1 lost nine days on flushing last year and float is one day, so we propose all four engineers stay on K2

What can still move 3 Nov, with the trigger, the effect and who decides

Risk	Trigger or evidence	Effect on 3 Nov	Owner	Decided by
Water source falls to a temporary truck	GC (Jason) reply due 21 Oct; municipal supply not yet confirmed	+3 days, ends 5 Nov	GC	21 Oct
Flushing starts after 24 Oct	K1 L2 slipped 9 days on the same step last year; float is 1 day	Day for day after the first day	GC	24 Oct
PAHU FAT goes to option A	Rayong lab, +2 weeks, +THB 180,000	Missed	K2	21 Oct
EPMS points list stays open	312 points unconfirmed by NV5; chased twice by 15 Oct	EPMS item cannot close; no date	NV5, K2	24 Oct
Site team drops from 4 to 2 engineers	**Two engineers were planned to move to K3 from 25 Oct, inside flushing week**	**Thinner cover for flushing and sampling**	**Allstewards (Ryan)**	**24 Oct**

The first three risks sit with GC and K2 and are decided by 24 Oct. The last one is ours: we propose keeping all four engineers on K2 until sampling is complete on 2 Nov, and releasing two to K3 after that.

Source: GC update 17 Oct; K1 L2 record; Allstewards manpower plan; Allstewards analysis

Confidential. Prepared for K2 project management

Water source and PAHU option B need K2's answer by 21 Oct; everything else runs to the L3 witness on 10 Nov

Decisions requested from K2, and the dated plan from today to the L3 witness

Decisions requested

Decision	From	By	If not
Accept PAHU FAT option B (calculation check, dew point verified at SAT) in place of a 120 kW rig test	Lim (K2)	21 Oct	+2 weeks, +THB 180,000; 3 Nov missed
Hold GC to municipal water for flushing; GC (Jason) to confirm the source	Lim (K2) with GC	21 Oct	Water truck: +3 days, ends 5 Nov
Raise the 312 unconfirmed EPMS points with NV5	Lim (K2)	24 Oct	EPMS item stays open without a date

Next 30 days

Date	Step	Who
21 Oct	Water source answer; PAHU option B accepted	GC (Jason); K2
22 to 23 Oct	UPS paralleling	Vendor
24 Oct	Flushing starts; K3 transfer held	GC; Ryan
31 Oct	Flushing complete	GC
1 to 2 Nov	Water-quality sampling	GC, Allstewards
3 Nov	L2 complete	Allstewards
10 Nov	Client L3 witness team on site	K2

Owner for the L2 date on the Allstewards side: Ryan Chen. We will send a one-line update after the 21 Oct answers and again when flushing starts.

Source: GC update 17 Oct; K2 RFS 30 Sep; Allstewards plan as at 18 Oct
